2045 On the Move 2020 Update

TMACOG

Last Updated:

12/10/2019

Project Start: Sun, 7/1/2018

Project End: Tue, 6/30/2020

TASK	PERSONS INVOLVED	PROGRESS	START	END
2045 Plan Process Table	Staff	100%	07/2018	08/2018
Plan Goals				
Update the 2045 goals from previous plan	Staff	100%	07/2018	08/2018
Task Force Approval of goals	Task Force	100%	08/2018	08/2018
Scenario Planning				
Land Use Scenario and incorporating jurisdiction's land use plans	Staff	100%	10/2018	10/2018
Employment Scenario	Staff	100%	10/2018	10/2018
"Possible Futures of TMACOG Region" Scenarios	Task Force	100%	11/2018	11/2018
System Facilities, Performance, and Needs Report				
System overview	Staff	100%	07/2018	12/2018
Present system overview to Task Force	Staff	100%	09/2018	12/2018
Update system performance section and progress since last plan	Staff	100%	12/2018	04/2019
Surveys for public input on needs	Staff	100%	11/2018	04/2019
Public meetings for input on needs	Staff	100%	02/2019	04/2019
Present survey and meeting results to Task Force	Staff	100%	04/2019	04/2019
Performance Targets and Measures				
Task Force approval of targets or setting of local targets	Task Force	100%	06/2018	09/2018
Tranportation Council and Board approval of targets and measures	Trans Council & Board	100%	09/2018	11/2018
Language drafted for the Plan	Staff	100%	11/2018	04/2019
Fiscal Plan				
Consult with State and Transit	Staff	100%	07/2019	08/2019
Draft projections report	Staff	75%	09/2019	09/2019
Task Force reviews projections	Task Force	75%	10/2019	10/2019
Draft Fiscal Plan to ODOT for review	ODOT	0%	04/2020	04/2020
Projects, Initiatives, and Policies				
Develop project lists, using targets & measures	Task Force	90%	04/2019	09/2019
Public meetings on project lists	Public	25%	10/2019	12/2019
Air Quality Conformity analysis	Staff	0%	01/2020	01/2020
Task Force reviews comments and approves final	Task Force	0%	02/2020	02/2020
Transportation Council approval of project lists	Trans Council	0%	03/2020	03/2020

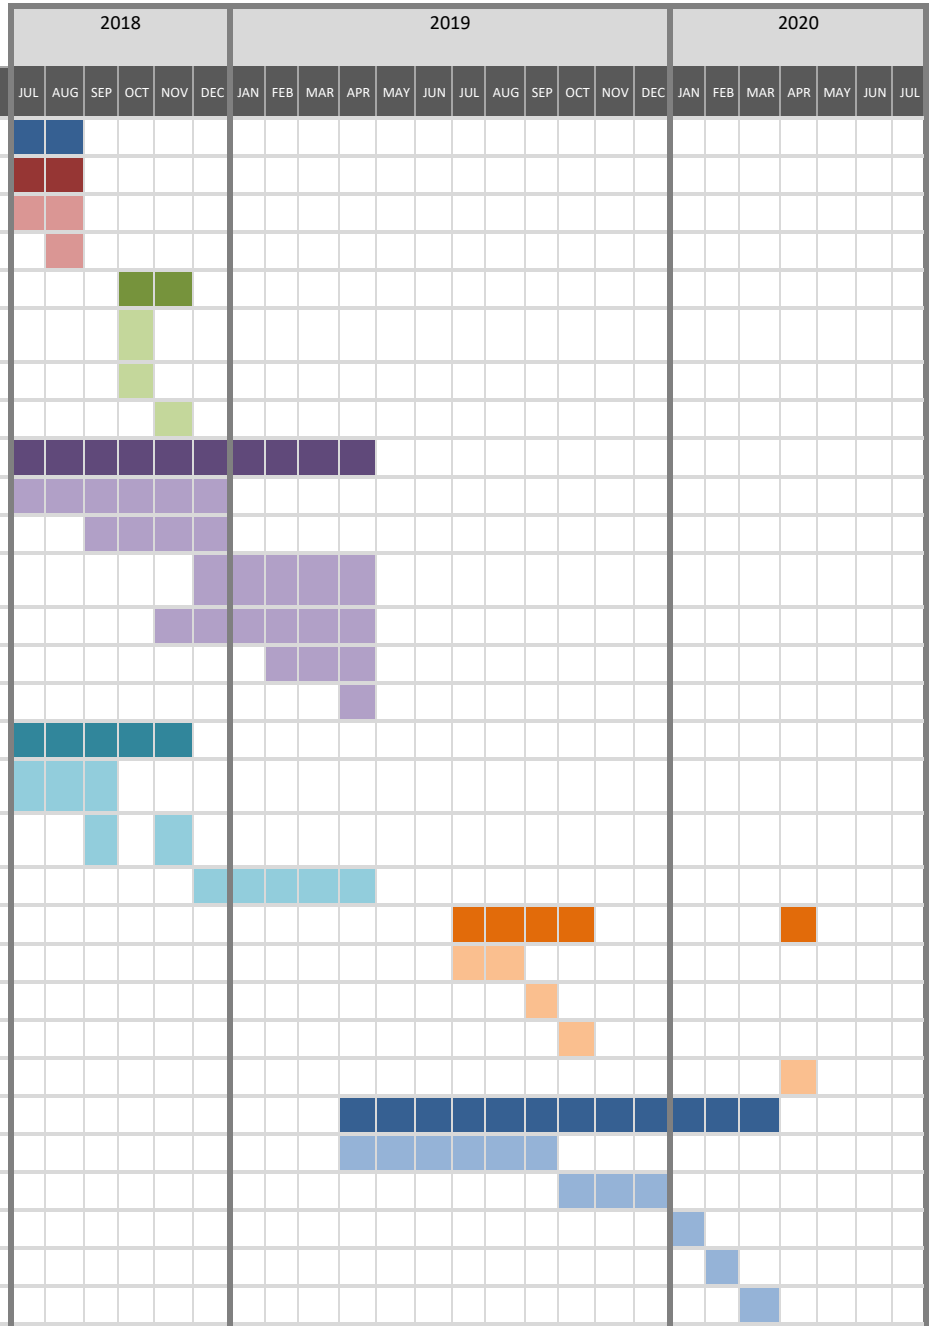

2045 On the Move 2020 Update

TMACOG

Last Updated:

12/10/2019

Project Start: Sun, 7/1/2018

Project End: Tue, 6/30/2020
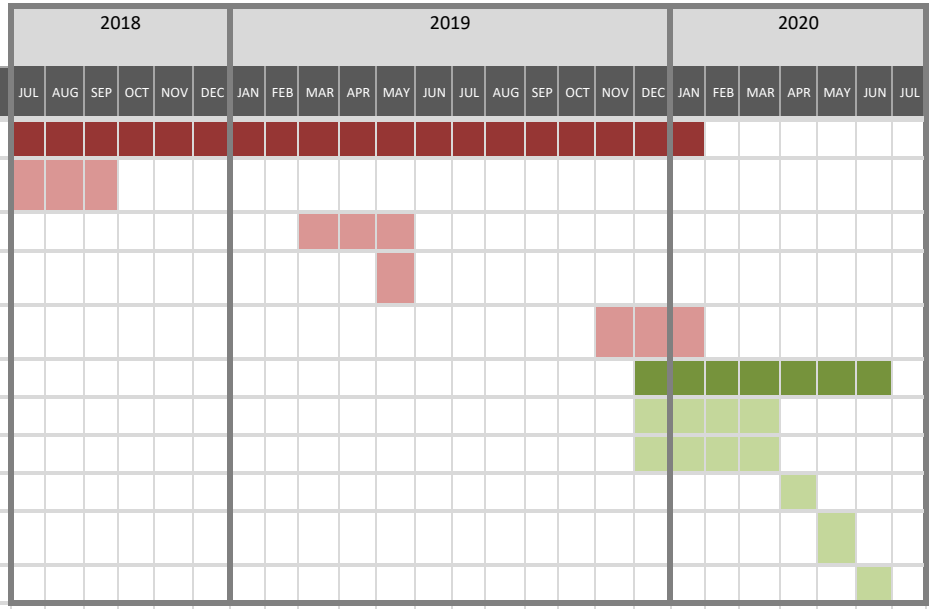
TASK	PERSONS INVOLVED	PROGRESS	START	END
Environmental and Stakeholder Consultation				
Inform stakeholders of plan development and opportunities to participate	Staff	100%	07/2018	09/2018
Solicit input on needs from major stakeholders	Staff	100%	03/2019	05/2019
Contact environmental agencies for comments and identify mitigation activities	Staff	100%	05/2019	05/2019
Review draft lists with environmental agencies and stakeholders	Staff	0%	11/2019	01/2020
Final 2045 Update Report				
Staff completes report	Staff	50%	12/2019	03/2020
Summary report completed	Staff	0%	12/2019	03/2020
Present to Task Force	Task Force	0%	04/2020	04/2020
Transportation Council & Executive Committee approve, submitted to ODOT	Trans Council	0%	05/2020	05/2020
TMACOG Board of Trustees approves Plan	Board	0%	06/2020	06/2020
